


LAB 2 – AGILE PROJECT MANAGEMENT USING JIRA

Clinical Trial Subject Recruitment Engine

NAME: G Harish reddy

SRN: PES1UG24AM366

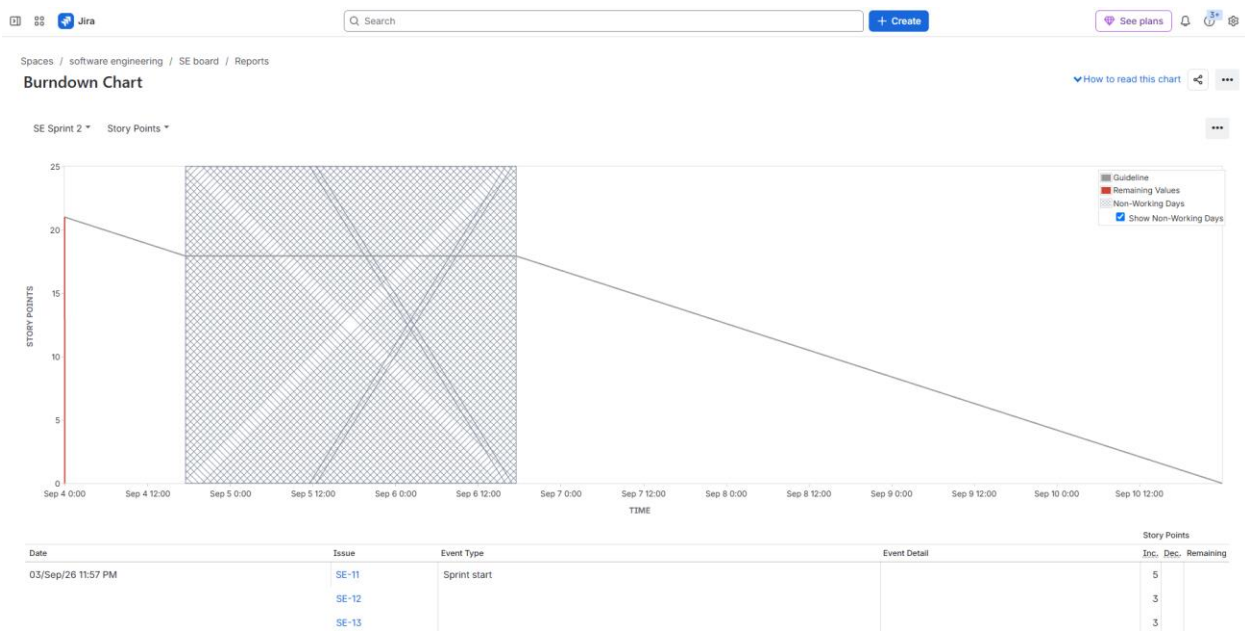

Jira

Search

Create

See plans

Spaces / software engineering

SE board

SummaryTimelineActive sprintsBacklogCalendarListFormsDevelopmentDocs

Search backlogVersionEpicQuick filters

Epic

No epic

Eligibility Evaluation

Informed Consent Management

Trial Visit Tracking

Recruitment Dashboard

Manual Review

Create epic

+ Create

0 work items | Estimate: 0

Backlog (10 work items)

4500Create sprint

Create a whiteboard to plan your work Try

SE-6 Submit Eligibility Survey

Eligibility ...

To Do

3

=

SE-7 Evaluate Candidate Eligibility

Eligibility ...

To Do

8

^

SE-8 Capture Consent Milestone

Informed ...

To Do

5

^

SE-9 Verify Consent Record

Informed ...

To Do

3

^

SE-10 Log Trial Visit

Trial Visit ...

To Do

5

=

SE-11 Flag Out-of-Window Visit

Trial Visit ...

To Do

5

=

SE-12 View Candidate Status

Recrutme...

To Do

3

=

SE-13 Filter Candidates

Recrutme...

To Do

3

=

SE-14 Flag Borderline Candidate

Manual R...

To Do

5

=

SE-15 Complete Manual Eligibility Review

Manual R...

To Do

5

=

+ Create

Jira

Search

Create

See plans

Spaces / software engineering

SE board

SummaryTimelineActive sprintsBacklogCalendarListFormsDevelopmentDocs

Search backlogVersionEpicQuick filters

SE Sprint 1

Add dates

5 work items

2400Start sprint

SE-6 Submit Eligibility Survey

Eligibility Evaluation

To Do

3

=

SE-7 Evaluate Candidate Eligibility

Eligibility Evaluation

To Do

8

^

SE-8 Capture Consent Milestone

Informed Consent ...

To Do

5

^

SE-9 Verify Consent Record

Informed Consent ...

To Do

3

^

SE-10 Log Trial Visit

Trial Visit Tracking

To Do

5

=

+ Create

5 work items | Estimate: 24

Backlog (5 work items)

2100Create sprint

Create a whiteboard to plan your work Try

SE-11 Flag Out-of-Window Visit

Trial Visit ...

To Do

5

=

SE-12 View Candidate Status

Recrutme...

To Do

3

=

SE-13 Filter Candidates

Recrutme...

To Do

3

=

SE-14 Flag Borderline Candidate

Manual R...

To Do

5

=

SE-15 Complete Manual Eligibility Review

Manual R...

To Do

5

=

+ Create

Jira

Search

+ Create

See plans

3

100

Spaces / software engineering

SE board

SummaryTimelineActive sprintsBacklogCalendarListFormsDevelopmentDocs

Search board

Version

Epic

Quick filters

Complete sprint

Group: Story

...

TO DO

5

Submit Eligibility Survey

Eligibility Evaluation

SE-6

Evaluate Candidate Eligibility

Eligibility Evaluation

SE-7

Capture Consent Milestone

Informed Consent Management

SE-8

Verify Consent Record

Informed Consent Management

SE-9

Log Trial Visit

Trial Visit Tracking

SE-10

+ Create

IN PROGRESS

DONE

5

Submit Eligibility Survey

Eligibility Evaluation

SE-6

Evaluate Candidate Eligibility

Eligibility Evaluation

SE-7

Capture Consent Milestone

Informed Consent Management

SE-8

Verify Consent Record

Informed Consent Management

SE-9

Log Trial Visit

Trial Visit Tracking

SE-10

Jira

Search

+ Create

See plans

3

100

Spaces / software engineering

SE board

SummaryTimelineActive sprintsBacklogCalendarListFormsDevelopmentDocs

Search board

Version

Epic

Quick filters

Complete sprint

Group: Story

...

TO DO

5

+ Create

IN PROGRESS

DONE

5

Submit Eligibility Survey

Eligibility Evaluation

SE-6

Evaluate Candidate Eligibility

Eligibility Evaluation

SE-7

Capture Consent Milestone

Informed Consent Management

SE-8

Verify Consent Record

Informed Consent Management

SE-9

Log Trial Visit

Trial Visit Tracking

SE-10

Reflection – Clinical Trial Subject Recruitment Engine

1. Did the story-point estimates reflect the actual effort?

The story points were estimated using the Fibonacci sequence. The 10 user stories were assigned between **3 and 8 story points**, with more complex activities such as evaluating candidate eligibility receiving higher estimates. Overall, the estimates provided a reasonable representation of the relative effort required for each story. During the sprints, the stories were completed successfully, suggesting that the estimates were suitable for planning the work. However, with more sprint experience, the team could improve future estimates by comparing planned story points with the actual effort taken.

2. Was the backlog well prioritized?

Yes, the backlog was prioritized according to the importance of the functional requirements. The **Eligibility Evaluation** and **Informed Consent Management** requirements were given higher priority because they are important for determining whether candidates can proceed in the clinical trial process. The remaining requirements, including Trial Visit Tracking, Recruitment Dashboard, and Manual Review, were given medium priority. This created a logical order for development and helped identify which functionality should be addressed first.

3. How did the sprint align with the overall plan?

The sprint plan was successfully followed. **Sprint 1** contained five user stories covering eligibility evaluation, informed consent, and trial visit tracking. The stories were moved through **To Do → In Progress → Done**, and Sprint 1 was completed successfully. The remaining five stories were then placed into **Sprint 2** and completed in the same way. This showed that the backlog could be divided into manageable groups of work while maintaining progress toward the overall Clinical Trial Subject Recruitment Engine requirements.

4. What insights did the Burndown Chart provide about team capacity?

The Burndown Chart provided a visual representation of how the remaining work changed as stories were completed. As the team moved the stories to **Done**, the remaining story points decreased. This helped demonstrate the team's progress during the sprint and provided an indication of how much work could be completed within a sprint. The chart also showed the usefulness of tracking work continuously rather than waiting until the end of the sprint to assess progress.

Conclusion

Overall, the Jira exercise demonstrated how functional requirements can be converted into **Epics and User Stories**, estimated using story points, prioritized, and organized into sprints. Completing two sprints and monitoring progress through the Burndown Chart provided a practical understanding of Agile backlog and sprint management. The exercise also showed that clear prioritization and regular tracking of completed work are important for managing development capacity effectively

